



# SAN BRUNO RECREATION & AQUATIC CENTER

Construction Advisory  
Committee Update

April 17, 2024





# AGENDA

1. Construction Update and Look Ahead Schedule
  - a) Project Information Update
  - b) Project Budget Update
  - c) Schedule Update
  - d) Progress Photos
2. City RAC Opening Preparation Updates
3. Questions

# Construction Update and Look Ahead Schedule



## PROJECT INFORMATION



**Start Date:** September 2021



**Project Completion:** Spring 2024 (Projected)



**Estimated Cost Completed To Date: 98.31%**



**EarthCam Link:** [https://share.earthcam.net/RecCenterBuild/rec\\_center\\_build/camera/view\\_1](https://share.earthcam.net/RecCenterBuild/rec_center_build/camera/view_1)



EarthCam Photo on 02/21/24



EarthCam Photo on 04/15/24


# Construction Update and Look Ahead Schedule

## *Project Budget Update*



- Approved Project Budget: \$62,290,288
- Total Expenses To Date: \$60,239,522.26
  - Total Construction Cost To Date: \$48,163,295
    - Including Contract Change Order: \$5,132,295

# SCHEDULE PROJECTIONS

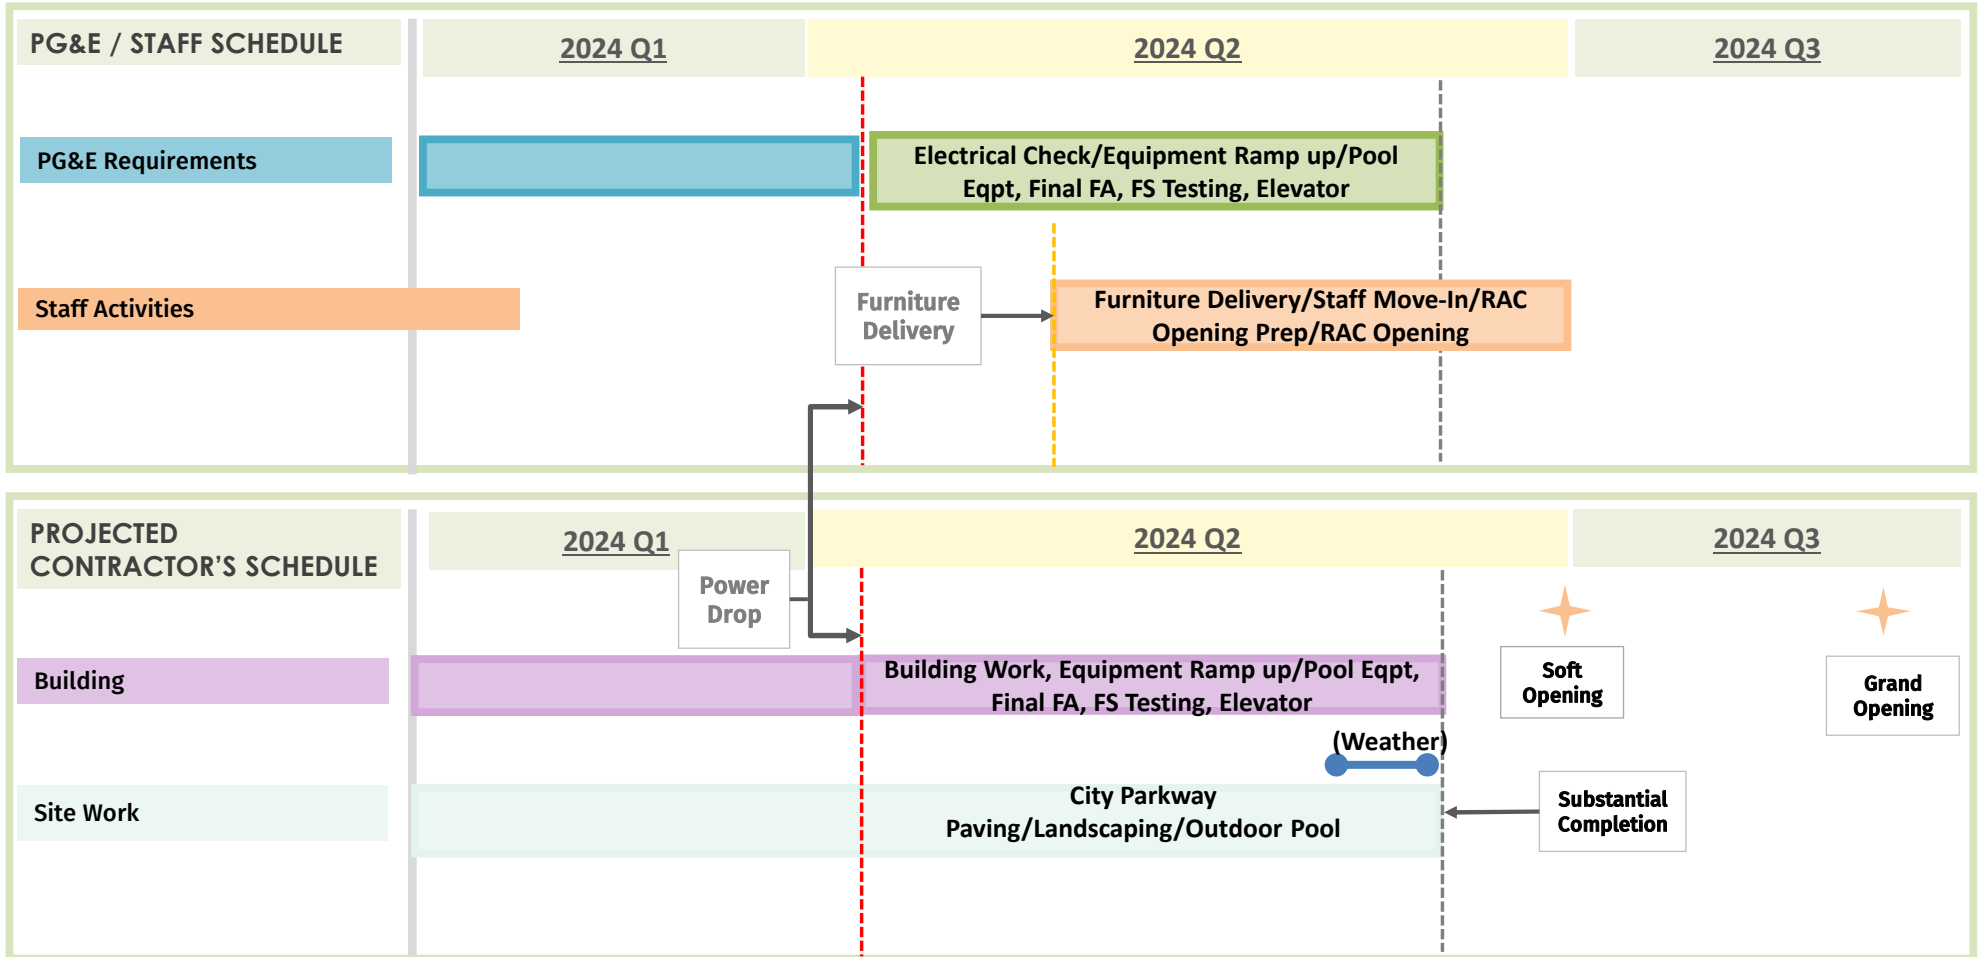

# Construction Update and Look Ahead Schedule

## *Progress Photos*



### SITE UPDATE



### OUTDOOR POOL / ROTARY PAVILION

# Construction Update and Look Ahead Schedule

## *Progress Photos*



### SITE UPDATE



KID'S PLAY AREA/PARKING LOT/CITY PARK WAY

# Construction Update and Look Ahead Schedule

## *Progress Photos*



### SITE UPDATE



PLAZA / MAIN ENTRANCE

# Construction Update and Look Ahead Schedule

## *Progress Photos*



### BUILDING UPDATE



Natatorium

# Construction Update and Look Ahead Schedule

## *Progress Photos*



### BUILDING UPDATE



**Community Hall**

# Construction Update and Look Ahead Schedule

## *Progress Photos*



### BUILDING UPDATE



Classrooms

# Construction Update and Look Ahead Schedule

## *Progress Photos*



### BUILDING UPDATE



**Fitness Room**

# Construction Update and Look Ahead Schedule

## *Progress Photos*



### BUILDING UPDATE



**Group Exercise Room**

# Construction Update and Look Ahead Schedule

## *Progress Photos*



### BUILDING UPDATE



Gymnasium

# Construction Update and Look Ahead Schedule

## *City Preparation Updates*



- Hiring Update
- Furniture and Fitness Equipment
- Soft Opening
- Grand Opening and Dedication
- Membership
- Rentals
- Programming

# Construction Update and Look Ahead Schedule

## *City Preparation Updates*



The banner features the City of San Bruno logo on the left. The main text reads "SAN BRUNO RECREATION & AQUATIC CENTER" in white on a blue background. Below this, in a larger font, is "SAN BRUNO IS HIRING!". At the bottom, it says "Part-time positions available!". To the right of the text is a photograph of a diverse group of people with their hands stacked in a circle, looking upwards.

We want YOU at the **NEW** Recreation and Aquatic Center!

- ✓ Flexible Hours
- ✓ Competitive Wages
- ✓ Fun & Fast-paced Environment
- ✓ Positions for All Experience Levels



A blue banner containing contact information and a QR code. On the left, there is a globe icon followed by the URL "sanbruno.ca.gov/RACJobs". Below that is an email icon followed by "SBCS@sanbruno.ca.gov" and a phone icon followed by "(650) 616-7180". On the right side of the banner is a square QR code.

# THANK YOU

[sanbruno.ca.gov/RecCenterBuild](https://sanbruno.ca.gov/RecCenterBuild)
